



Sewer Improvement Update

Susan Banzon and Ryan Westra
City of Hackensack Project Managers

City's CSO Surcharge Construction Status


Clay Street Sewer Separation:

Progress Recap

- 1,670 Linear feet of Stormwater infrastructure has been installed since the start of the project.
- Substantial completion is expected by April 2022.

Active Construction:

- PSE&G performed relocations of overhead electric and Suez Water has relocated water on Camden Street in areas of conflict.
- PSE&G Gas and Suez Water performed relocations on Union Street in areas of conflict.
- Contractor is currently installing sanitary sewer improvements on Clay Street.
- Contractor is scheduled to start the heavy clean, inspection, structural repairs and lining of the existing sewer throughout the project limits this month.
- 1,600 LF of box culvert is in production and anticipated for delivery in October.

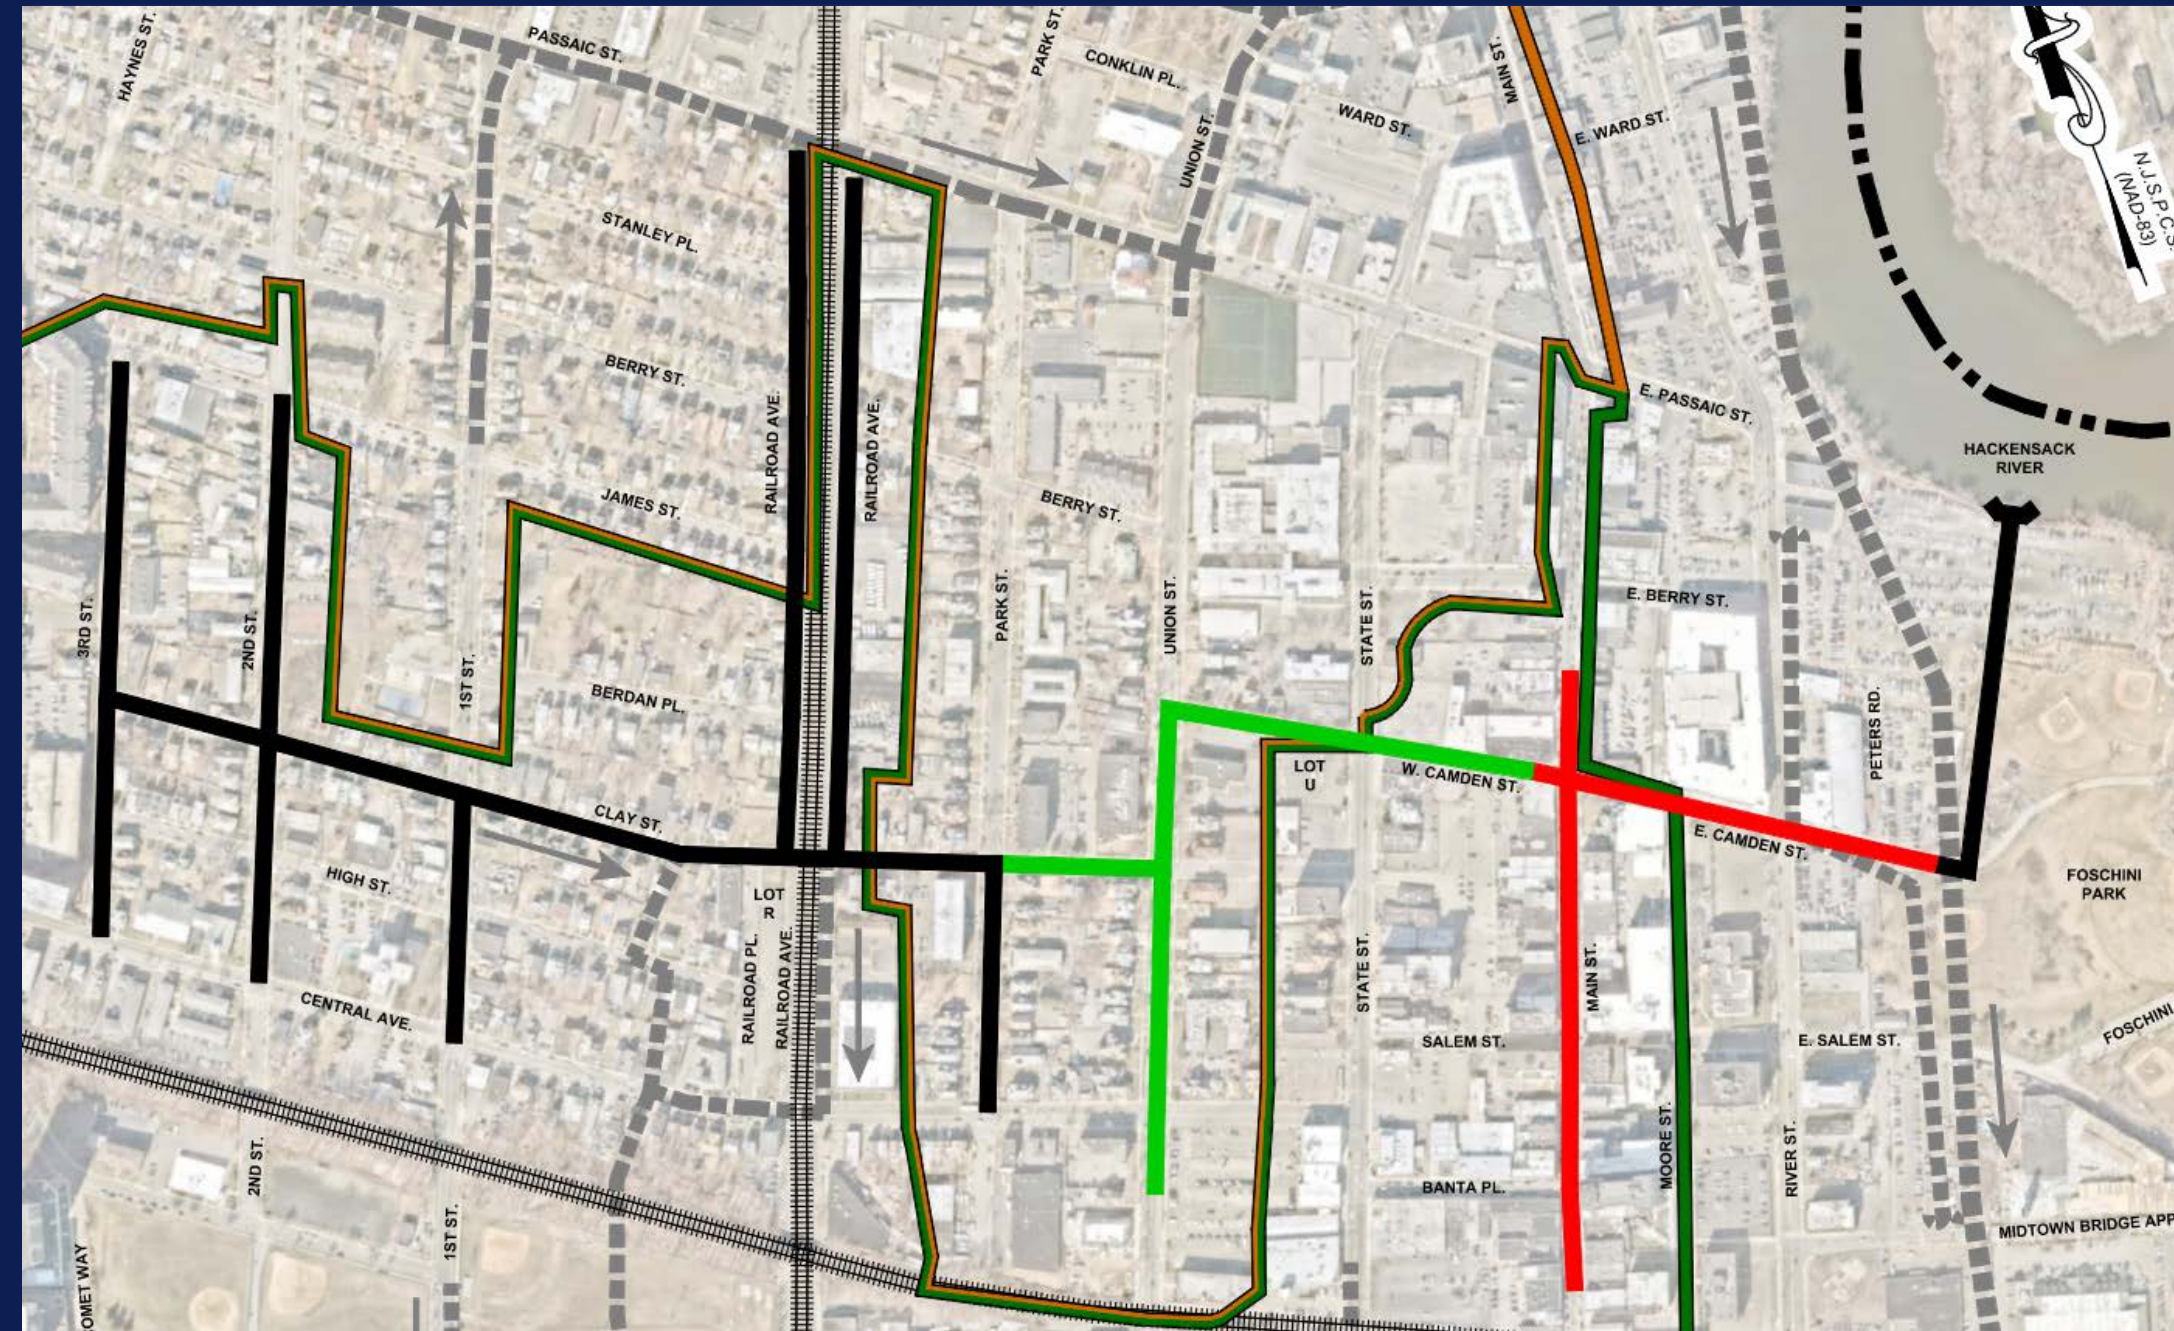

Clay Street Sewer Separation Contract Status

Contract 2:


- Approved by NJDEP Land Use
- Approved by Office of Equal Opportunity and Public Contract Assistance
- Awaiting NJDEP Authorization to Advertise
- Awaiting easement acquisition

Contract 3:

- Approved by NJDEP Land Use
- Under review by NJ Transit for occupancy permits
- Under 90% completion review with the City

Contract 4:

- Partially approved by NJDEP Land Use
- Approaching 60% completion review

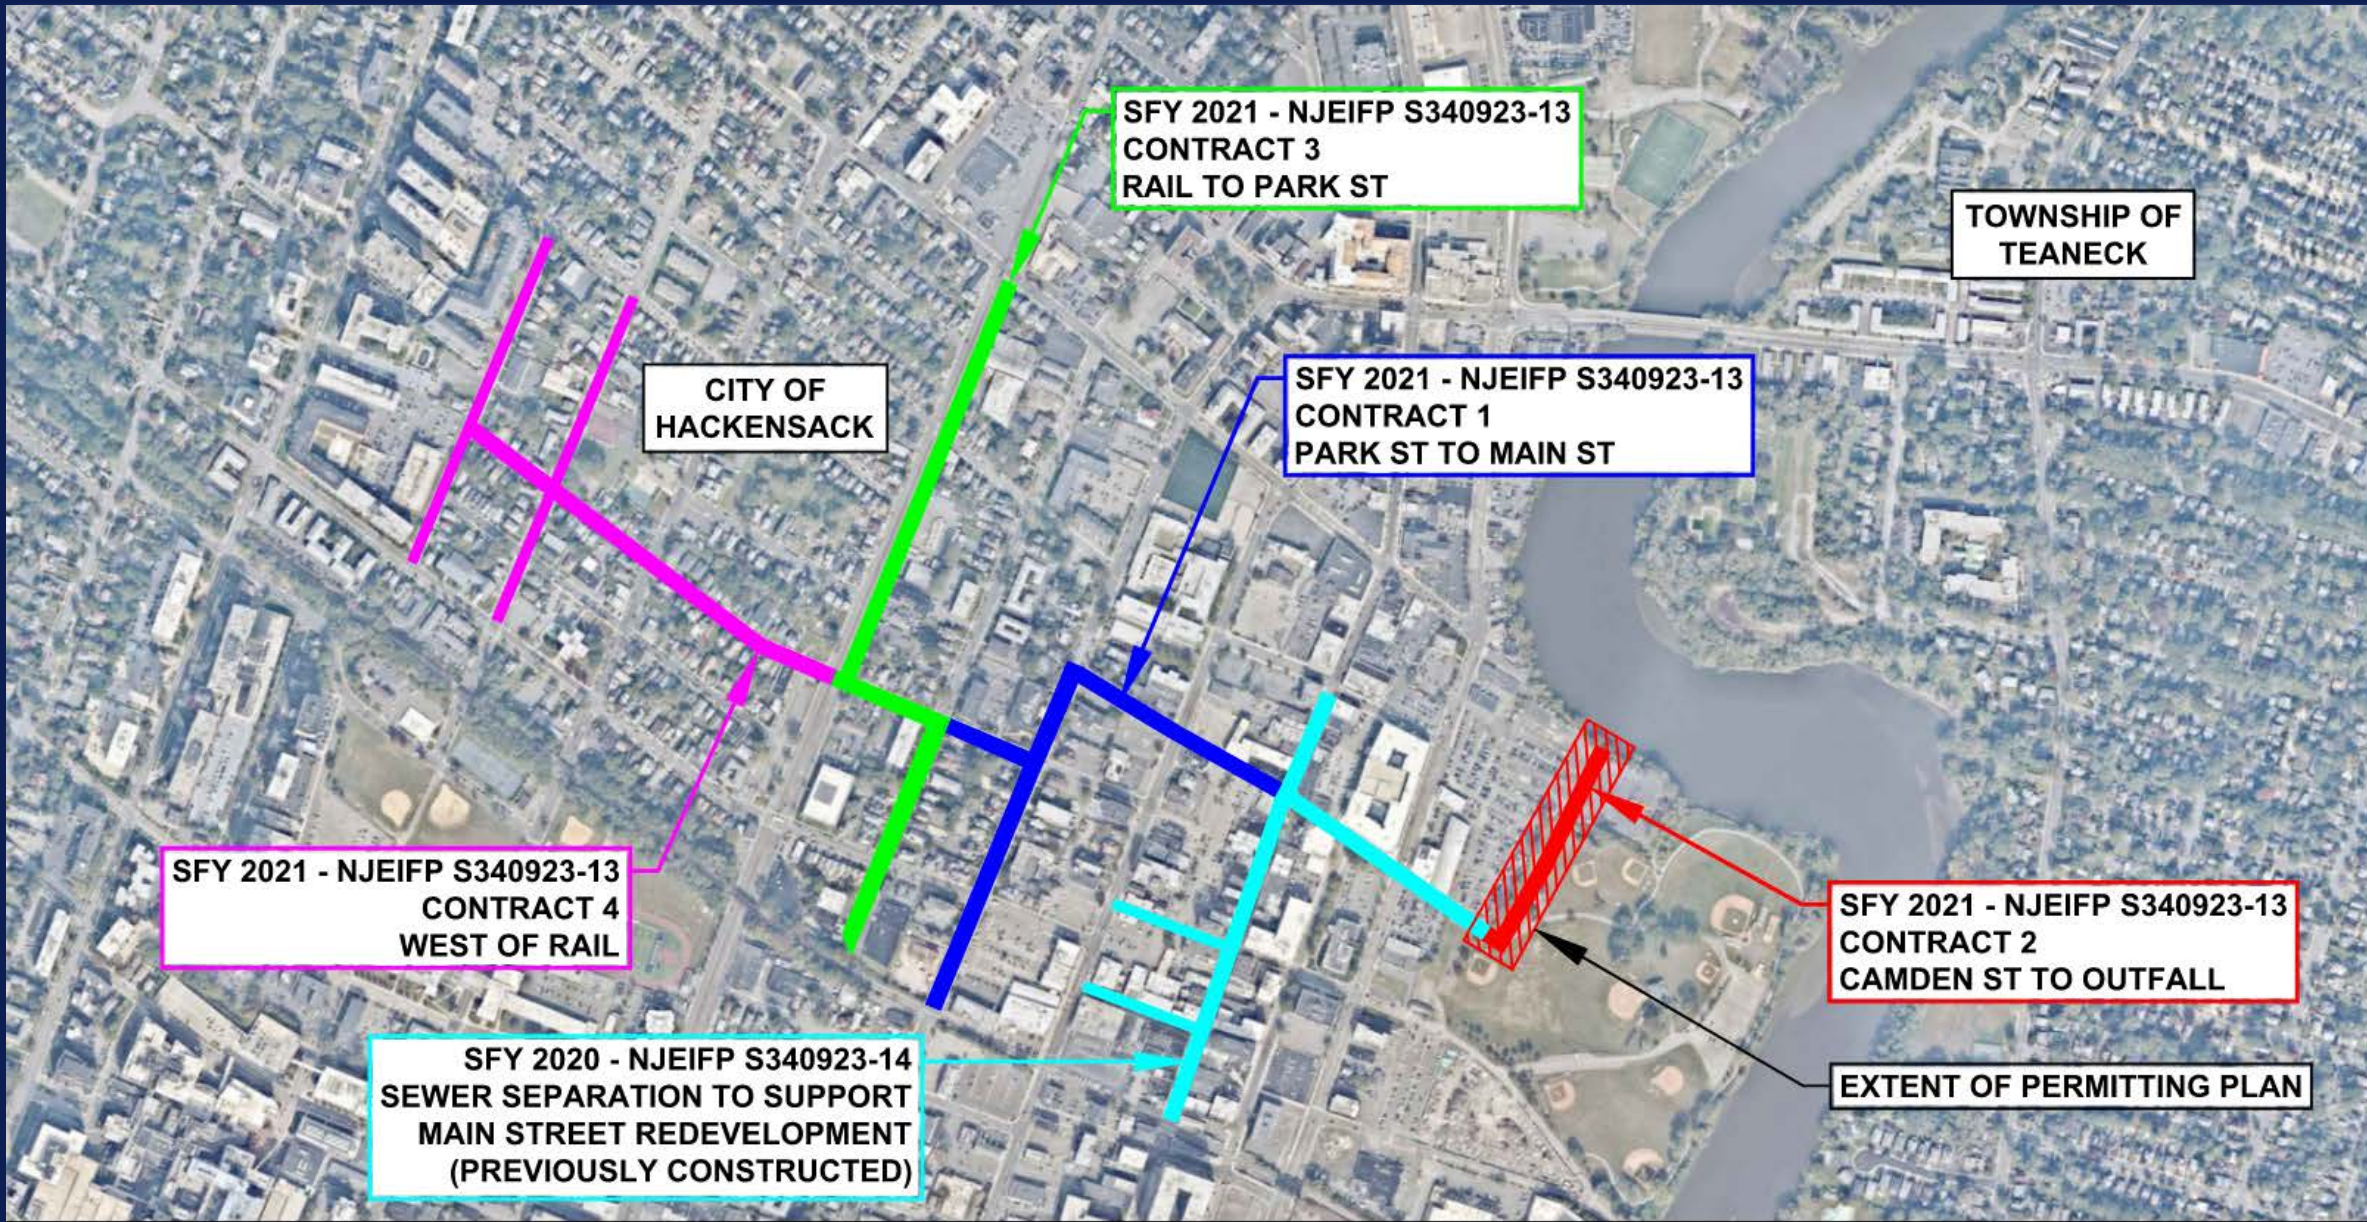

HUMC Development Agreement:

- The City has obtained financial commitment and hard infrastructure box culverts from HUMC to support the City's BRIC grant application and in lieu of HUMC construction. The box culverts will be installed under the Clay Street Separation project. A resolution amending the HUMC's RDA is on the agenda this evening.
