


CITY CONSTRUCTION STATUS – CSO SEPARATION STATUS



PROJECT	DATES	ACRES of STORMWATER DIVERTED from COMBINED SEWERS
Initial Main St. Contracts	2015-2019	15.5
Main St. Contracts 1+2	2020-2022	36
Clay St. Contract 1	2021-2023	12
Clay St. Contract 2	2022-2023	--
Clay St. Contract 3	2022-2023	8
Record Site Outfall	2021-2023	--
Anderson Drainage Area	2023-2025	22.5
W. of Rail Contract 1 TWA Extension currently under DEP Review	Pending: 2026 September Bid October Award	14
West of Rail Contract 2	Pending: 2026-2027	21

CITY CONSTRUCTION STATUS – CSO SEPARATION STATUS

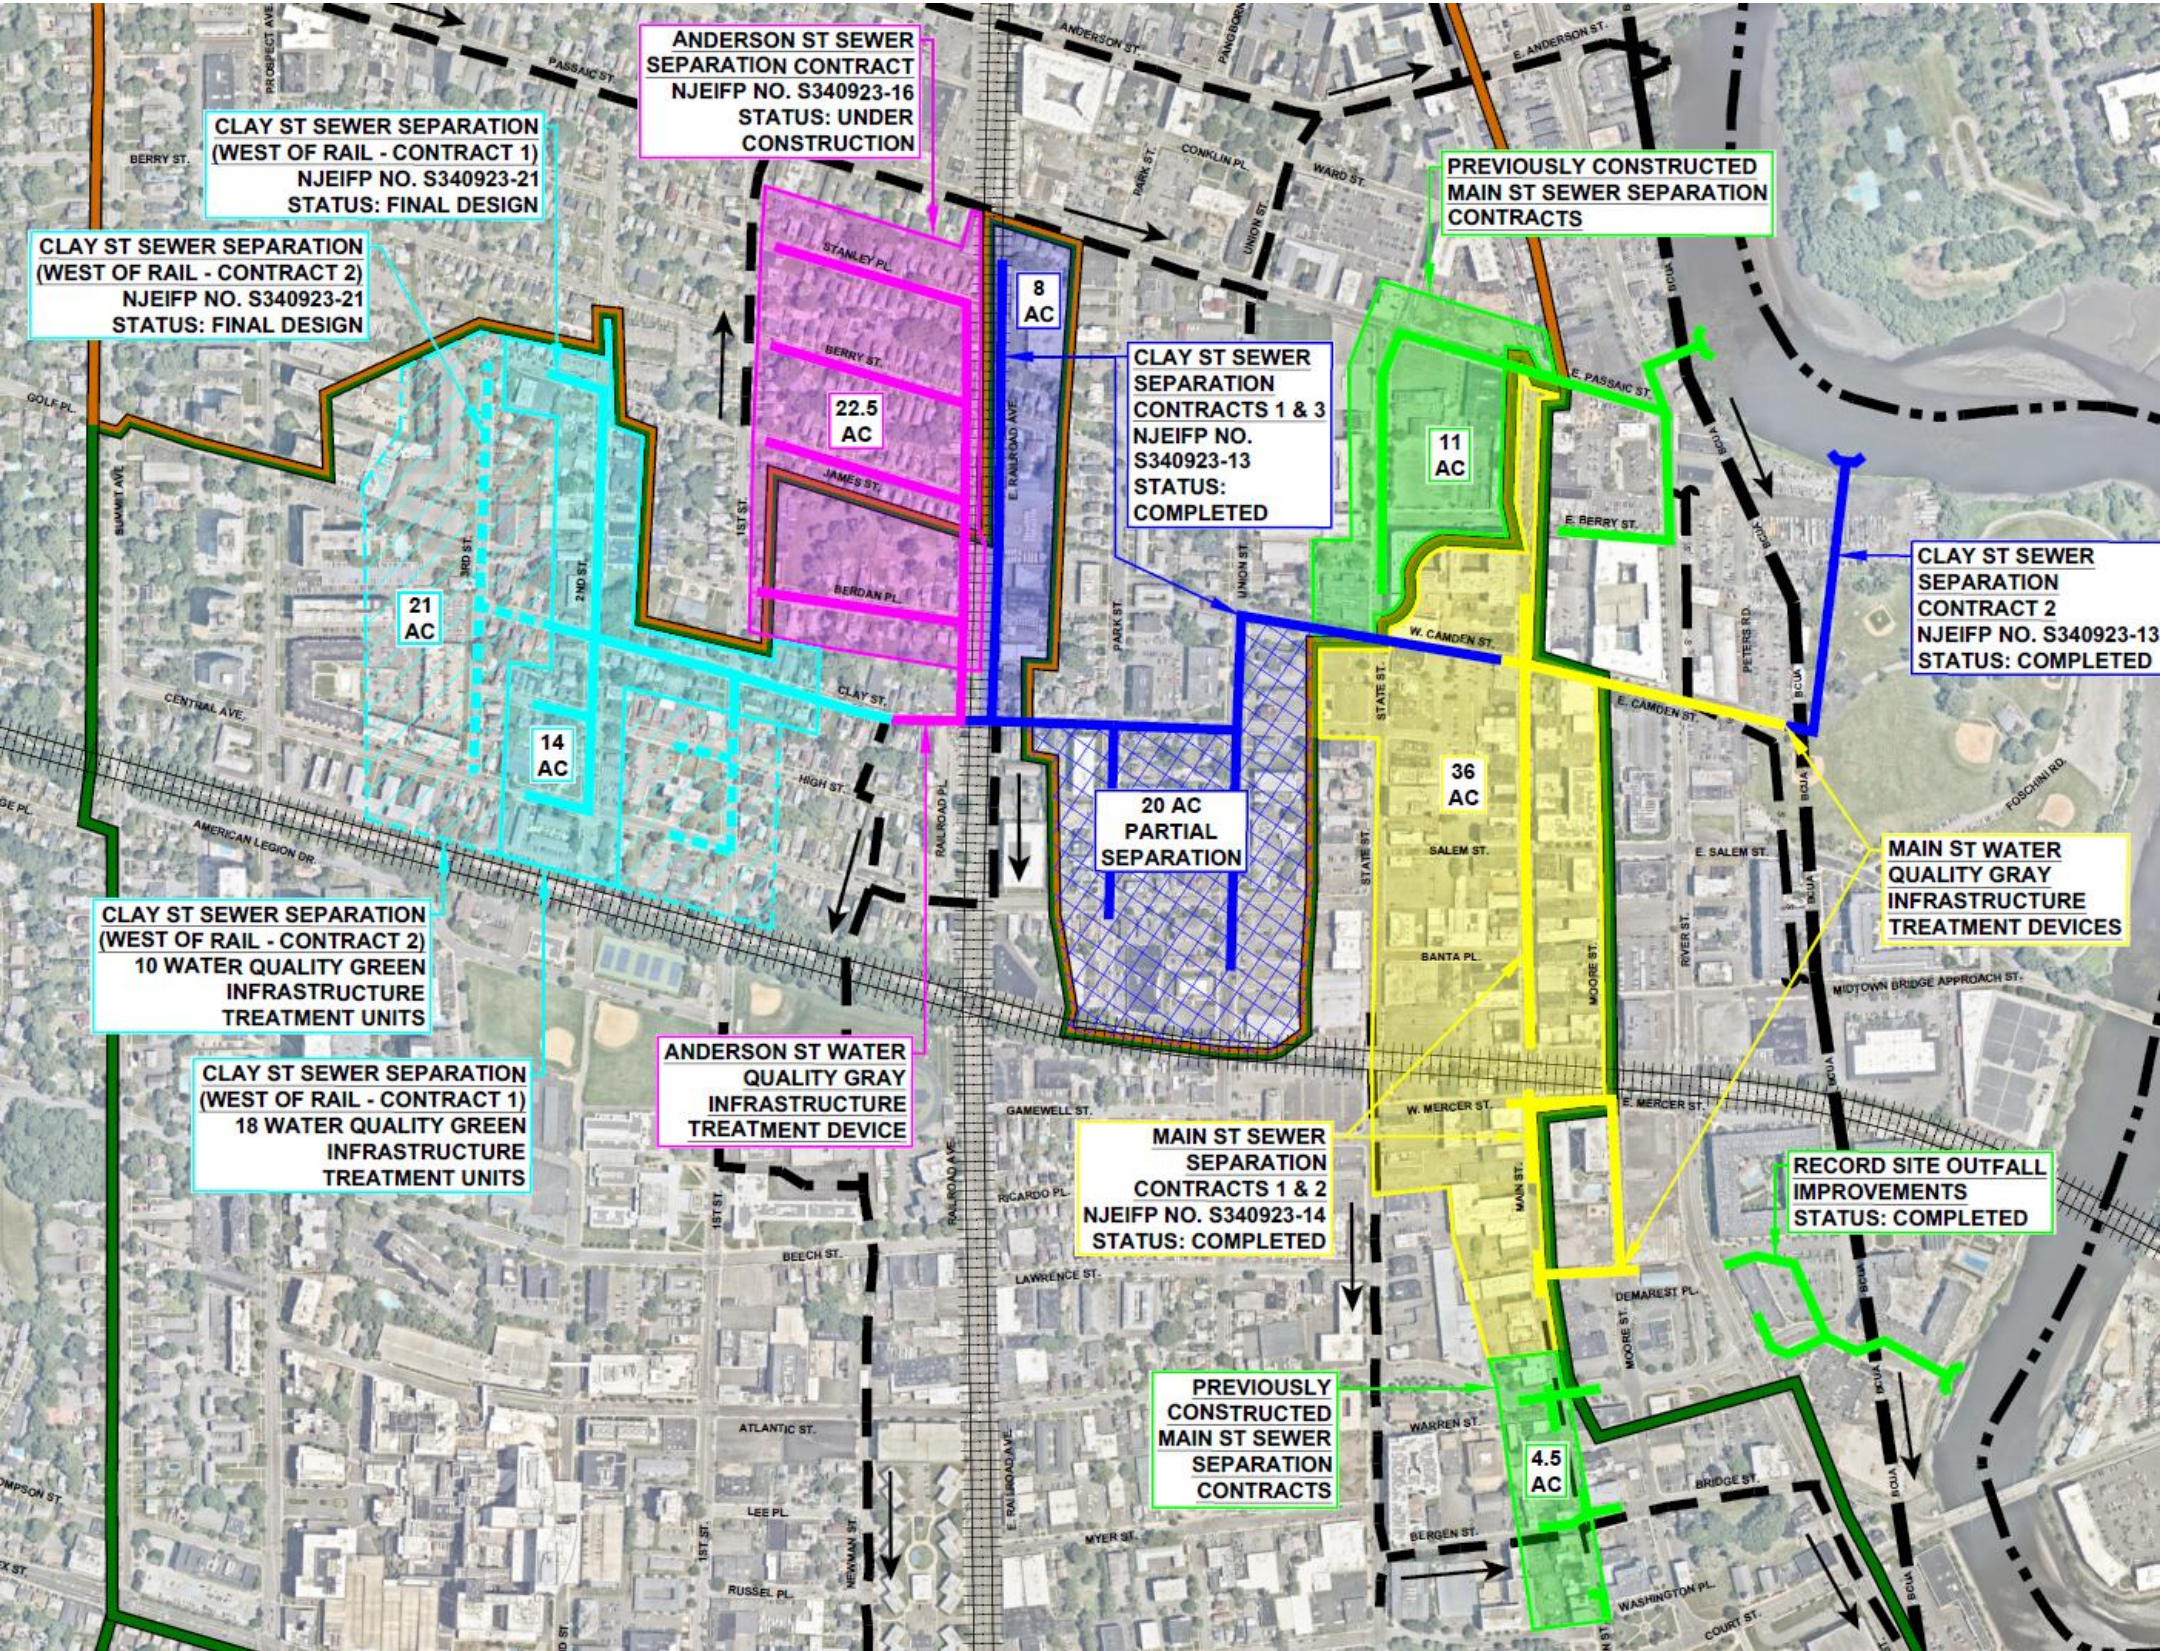

CITY'S NEXT SEWER SEPARATION PROJECTS	GREEN INFRASTRUCTURE WATER QUALITY UNITS
<i>West of Rail Contract 1</i>	<i>18 tree filters</i>
<i>West of Rail Contract 2</i>	<i>10 tree filters</i>

West of Rail Contract 1

Bid Advertisement Date: 9/14/2026
Bid Closing Date: 10/14/2026
Bid Opening Date: 10/14/2026
Contract Award Date: 10/20/2026

